

Experience comes from the mistakes we make;

wisdom
comes from
the mistakes
we learn from
others.



Support the implementation of the AMR National Action Plan in Tunisia using One Health Approach

(AMR-MPTF-TUNISIA)

Timeframe: initially planned for June 2023

Budget: 999 269 USD

• **FAO**: 374 197

• **WHO**: 261 893

• WOAH: 262 367

UNEP: 102 720















Ministère de

l'Environnement-Tunisie 💝

السیّد حبیب عبید یتسلّم مهامه علی رأس وزارة 📗

حبيب عبيد، وزير البيئة اليوم الاثنين خلفا للسيّدة ليلى الشيخاوى وكب تسليم وتسلّم المهام الذي تم





Latest update 16:48 Tunis

-1: -11: -

Home

Politics

وتسلّم المسام بحر

Economy

Regions



PARTAGER

mi

PAR LECONOMISTE MAGHRÉBIN | 1 MIN LECTURE |


SAUVEGARDER

2024/08/26 AT 7:42 PM













Support the implementation of the AMR National Action Plan in Tunisia using One Health Approach

(AMR-MPTF-TUNISIA)

Timeframe: May 2024–December 2025

(initially planned for June 2023)

Budget: 999 269 USD

• **FAO**: 374 197

• **WHO**: 261 893

WOAH: 262 367

• **UNEP:** 102 720
















Partners






















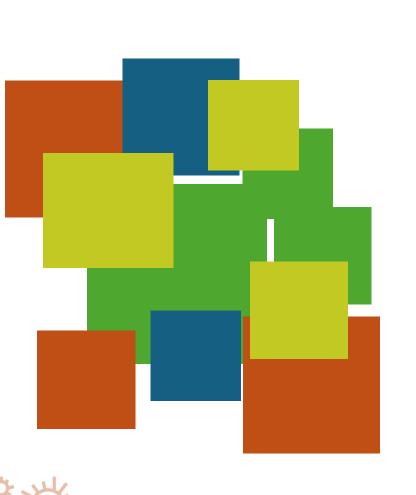

4 consultations

TS/s-COS2024/1

Support the establishment and functioning of the national inter-ministerial AMR steering committee in Tunisia.

TN/s-COS2025/1

Support the national AMR surveillance system in Tunisia for better monitoring planning, data collection, processing and dissemination to key stakeholders

TN/S-COS2025/2


Assess current legal and institutional frameworks governing AMR in human health, animal health, plant protection and environment sectors and propose the necessary amendments to meet AMR challenges using quadripartite tool -

Revise the NAP to include environmental health and plant health and to update activities

TN/s-COS2025/3


Assess, design and support implementation of traceability system of antimicrobials in human health, animal health, plant protection and environment sectors.

Advocate for the development of an updated AMR training modules in veterinary, medical, environment, dentistry, pharmacy and paraprofessional



Event- awarness day

- An event is scheduled to take place alongside WAAW 2025 in November, jointly organized by all project agencies.
- Planning and brainstorming on activities are currently underway.
- The venue will be the Cité des Sciences in Tunis, a popular and wellvisited location for children, offering ample space and rooms.
- The event is likely to be held on a weekend to maximize attendance.
- Activities will include scientific conferences, children's workshops (such as drawing, puzzles, singing, and creative arts), exhibition stands, and a showcase of the project's highlights.



TS/s-COS2024/1


Support the establishment and functioning of the national inter-ministerial AMR steering committee in Tunisia.

Ongoing activity

• First deliverable completed: diagnostic report on the current situation, including the identification of coordination and communication gaps among stakeholders and the mapping of all parties involved in AMR in Tunisia.





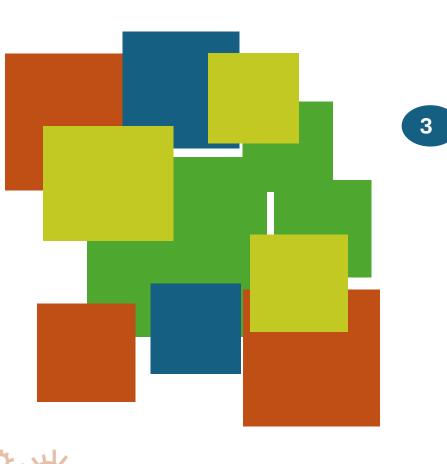


TN/S-COS2025/2

Assess current legal and institutional frameworks governing AMR in human health, animal health, plant protection and environment sectors and propose the necessary amendments to meet AMR challenges using quadripartite tool-

Revise the NAP to include environmental health and plant health and to update activities

Consultation launched:

A single application

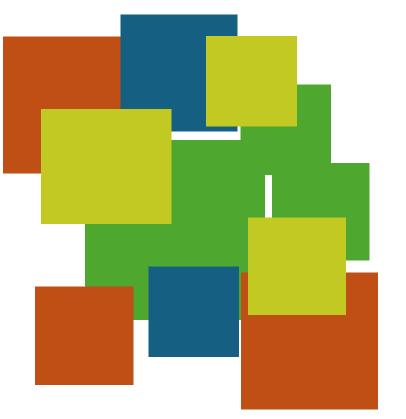

TN/s-COS2025/3

Assess, design and support implementation of traceability system of antimicrobials in human health, animal health, plant protection and environment sectors.

- Launch ongoing: published
- Challenges: limited budget.

Unfruitful







Before Project Launch

Before Project Launch - Key Elements:

- Conduct a detailed situational analysis: map existing initiatives, gaps, and available human and institutional resources. This enables effective planning and optimal resource allocation
- Identify specific needs for each sector: human health, animal health, environment, and food security to tailor interventions to local realities
- Define strategic partners early on and clarify their roles and responsibilities to ensure clear leadership and effective coordination
- Secure stakeholder engagement before starting upstream consensus facilitates smoother implementation



Balance donor requirements (MPTF) with national priorities, aligning local needs with international frameworks.

During the Call for Proposals:

Develop the project proposal through a participatory process: engage ministries, technical agencies, partners, and civil society to ensure relevance and ownership.

Be realistic and build on solid foundations: a modest but feasible project is better than an overly ambitious, unachievable one.

Align the budget with planned actions, accounting for market fluctuations (equipment, consultants).

Do not treat the budget as a 'cake to be divided': each agency uses its capacity to maximize collective impact.

Consider national legal frameworks — only propose activities compliant with national law to avoid implementation failure

During the Call for Proposals:

- Advocate with national decision-makers to promote cross-sectoral collaboration under One Health — a constant but essential challenge
- Consider inviting a colleague involved in a similar project from another country in the region to provide advice and recommendations.
- Keep in mind that the person responsible for implementation (coordinator, focal point, etc.) may not be the one who drafted the document; therefore, activity descriptions should be written clearly, precisely, and explicitly.





What happens after the project? How will the country continue its fight against AMR on its own?

"Wouldn't a sustainability or exit strategy be essential to preserve achievements and ensure continuity?"

Shouldn't monitoring and evaluation be considered from the very beginning to track progress, capture best practices, and guide future decisions?

Thank you!



12, rue de Prony, 75017 Paris, France T. +33 (0)1 44 15 19 49 F. +33 (0)1 42 67 09 87

woah@woah.org www.woah.org

Facebook

Twitter

Instagram

LinkedIn

YouTube

Flickr









